

# Hawai'i Department of Transportation Highways Maui District

West Maui Update on Fire and Storm Damage Repairs

---



June 3, 2026

# Wildfire Repairs

## Honoapiʻilani Highway Drain Line Improvements

Between Shaw Street and Leialiʻi Parkway

- Work ongoing
- Anticipated Completion: End of June/Beginning of July



# Wildfire Repairs

## Honoapiʻilani Highway

### Guardrail Work

Between Leialiʻi Parkway  
and Kapunakea Street

Construction Start: Week of May 18

Construction Complete: Mid-October



# Wildfire Repairs

## Emergency Evacuation Route near Lahainaluna High School

HDOT re-examining the route for  
improvements

2.5-mile route from  
Lahainaluna fire lane to  
Lahaina Bypass



# Wildfire Repairs

## Honoapiʻilani Highway Traffic Signal Replacement

Five signals between Shaw Street and Hinau Street

- Estimated Start Date: July 2026
- Anticipated Completion: December 2028



# Kona Low Emergency Repairs

## Honoapiʻilani Highway Landslides (MM 33 - 36)

- Scaling on the mauka side is complete
- Work on makai side is anticipated to start in June and take 5 months



# Kona Low Emergency Repairs

## Honoapi'ilani Highway Rockfall Fencing (MM 10.25 - 10.80):

- Project out to bid by end of 2026
- Night work
- Approximately 200 linear feet of fencing to be installed
- Fence heights from 75 to 150 feet



## Drain Line Replacement along Keawe Street:

- Project to start early June
- Expected to be completed by end of June/beginning of July



# Honoapiʻilani Highway Traffic Emergency Zone

Mile Marker 13.75-14.5

- Completion pending Hawaiian Telcom relocating their line and pole
- Once complete, remaining work should be done within two weeks




# Honoapiʻilani Highway Improvements

Ukumehame to Laniupoko

Contract Award: August 2026

Construction Start: Mid/Late 2027

Construction Complete: Mid/Late 2031

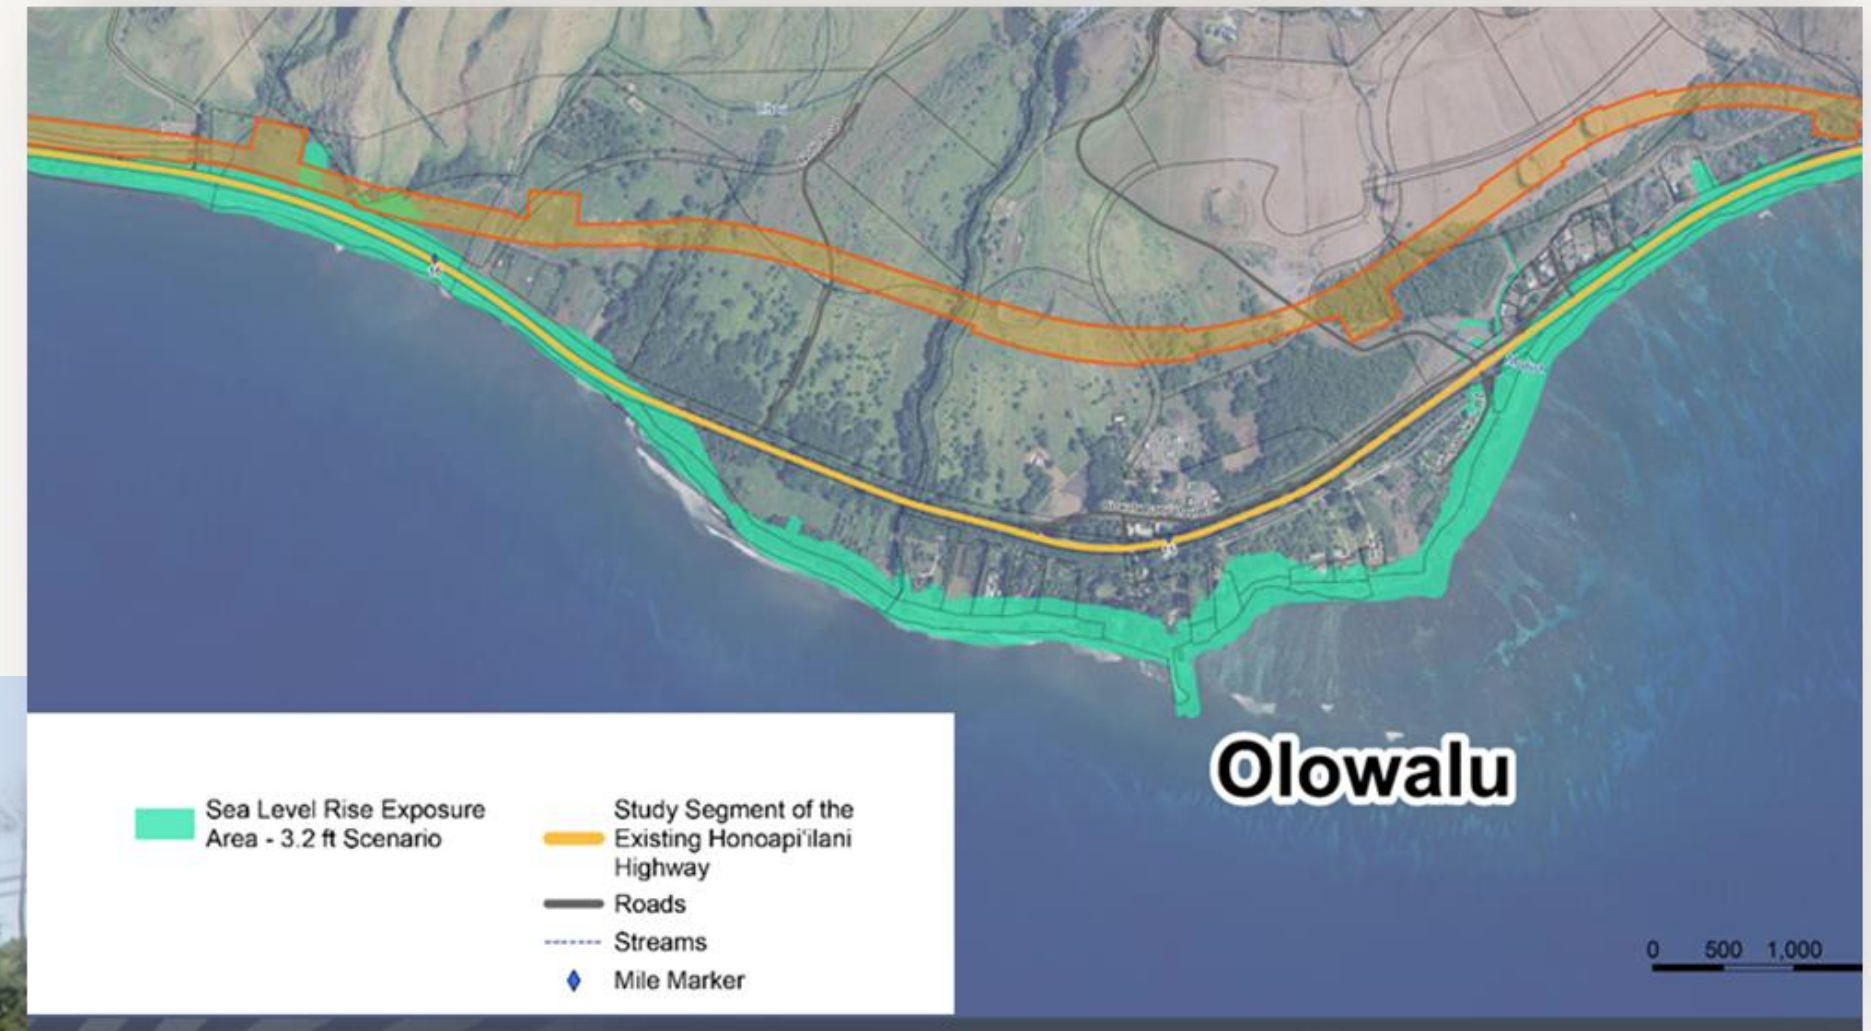

Visit:

[www.honoapiilanihwyimprovements.com](http://www.honoapiilanihwyimprovements.com)

# Lahaina Bypass 1C

**Keawe Street to Pu'ukoli'i**

Starting Preliminary Environmental Studies

Estimated Construction Start: Mid/Late 2028

Construction Complete: December 2030

